COREPROMA
SOLAR FARM PROJECT PLATFORM · PREPARED FOR ETHICAL POWER

PROPOSAL & QUOTATION · V0.3 DRAFT

The Ethical Estimation Engine.

Design, build, hosting and support of the platform that replaces the manual, document-driven tendering process: one governed workflow from project capture to a defensible, risk-priced estimate.

Estimating core live mid-December 2026 · January hypercare · signature needed by end August

£250,000

Capped development under shared ownership · Phase 1 bespoke build

Hard cap on Phase 1 development, including six months of Azure hosting. Requires the shared ownership structure in Section 12.

01 Executive summary

READ THE HONEST VERSION FIRST

Coreproma proposes to design, build, host and support the platform Ethical Power refers to as the Ethical Estimation Engine. It captures a project through a guided wizard, quantifies its risks as named budget provisions, generates a bill of materials and cost estimate from a controlled rate library, and reports risk and cost exposure to management and investors. Delivery is phased. **Phase 1, to end 2026:** the estimating core plus the delivery and governance workspace, the latter not bespoke development at all but Coreproma's existing, field-proven Jobs Tracker platform, extended for solar project delivery and sold as a per-user monthly subscription. Go-live mid-December, followed by a January hypercare window. **Phase 2, Q1 2027:** supplier and third-party management, full management and investor reporting, and rate intelligence.

The extra weeks to December are not slack: scope moved in with the date — HONEST

Moving go-live from mid-November to mid-December buys about four weeks. Phase 1 now also has to deliver the Jobs Tracker solar projects extension and the governance integration, which the November plan deferred. Net float is close to zero, and the date holds only if the contract is signed by end August. UAT and cut-over cannot run in the week of 25 December: mid-December is the real freeze, and January is hypercare, not build.

The engine is only as good as the rate data Ethical Power supplies — HONEST

Coreproma builds the calculation engine; it cannot invent the unit rates. The QS and procurement team must hand over the rate library early. Placeholder rates can never yield a green confidence score.

Grid-connection cost is excluded by design — BY DESIGN

The DNO grid-connection cost, potentially £200k to £10M+, is never modelled. It is obtained from the DNO. This is a feature, not a gap: modelling it would produce dangerous mispricing.

What Ethical Power is buying

Phase 1 · to end 2026
Estimating core plus the Jobs Tracker delivery and governance workspace. Live mid-December.

Phase 2 · Q1 2027
Supplier and third-party management, full reporting, and rate intelligence.

Jobs Tracker workspace
Phases and governance on the existing platform, per user per month, outside the new structure.

Hosting & identity
Coreproma-managed Azure, sign-in through Ethical Power's own Entra ID with MFA.

Support & ownership
12-month support contract with SLAs, and a shared ownership structure that caps the build.

THE COREPROMA SOLAR FARM PROJECT WORKFLOW · MODULES B1 TO B7, INCLUDING THE RISK REGISTER


Coreproma

Solar Farm Project Workflow

Operational Architecture & Governance Framework — incl. Risk Register

ethical power
PREPARED FOR ETHICAL POWER

REFERENCE DIAGRAM

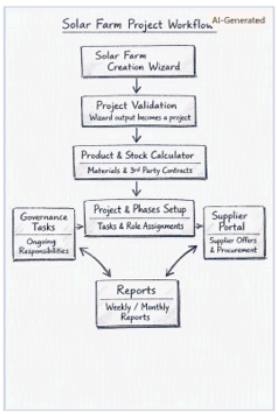

Hand-drawn workflow sketch provided by Ethical Power

WHY RISK QUANTIFICATION MATTERS

- Each risk gets a named £ provision, not a % contingency
- Information gaps priced explicitly
- Clients see exactly what risks are costed & why
- Provisions flow into B3 as named budget lines
- Live status tracked through B6 & B7 during delivery

B1 — Solar Farm Creation Wizard

Automated workflow capturing technical, regulatory, environmental & financial inputs. Integrates GIS terrain data (GEOALT / Google Maps), road access, fencing, and panel layout.

PROJECT INITIATION & DATA CAPTURE

VALIDATES

B2 — Project Validation

Converts wizard output into a formal project record. Automated feasibility — site suitability, regulatory compliance, budget envelope, technical sign-off.

FEASIBILITY & COMPLIANCE CHECK

RISK ASSESSMENT

B2b RISK — Risk Register & Provisions

CAPTURES PER RISK
- Risk type & category
- Status: Known / Potential / Info Gap
- Likelihood: High / Med / Low
- Named £ cost provision
- Basis of estimate

RISK CATEGORIES
- Ground & geotechnical
- Information gaps (surveys)
- Grid connection
- Planning & permitting
- Access, logistics & environment

RISK QUANTIFICATION & BUDGET LINK

PROVISIONS FEED INTO BUDGET

B3 — Product & Stock Calculator

Auto-generates full bill-of-materials with risk provisions included as named budget lines — panels, piles, cabling, inverters, mounting, plus itemised risk contingencies.

MATERIALS, 3RD-PARTY & RISK BUDGET

PLANS

B6 — Governance Tasks

Tracks risk status during execution — confirms provisions spent or released.

B5 — Project & Phases Setup

Phased plan — milestones, tasks, assignments & dependencies.

CENTRAL HUB

B4 — Supplier Portal

Pre-qualified suppliers submit offers. Validated on price, lead time & ESG.

B7 — Reports

Live risk register status — which provisions spent, which resolved, remaining exposure. Weekly & monthly for management and investors.

MANAGEMENT INSIGHTS & RISK TRANSPARENCY

Main flow · Risk Register (B2b) · Bidirectional (B5↔B6) · Procurement (B5→B4) · Reporting (→B7) · Data flow

COREPROMA · Solar Farm Platform · Confidential — Prepared for Ethical Power

Wizard output validates into a governed project record; risks feed the budget as named provisions; the cost calculator plans delivery through the phases hub, governance tasks and supplier portal; reports close the loop for management and investors.

03 Scope of development · the estimating core

PHASE 1 · LIVE MID-DECEMBER

B1 · Solar Farm Creation Wizard

A guided, ten-step wizard for a commercial user, not an engineer. Live cost panel and confidence flags from step 4.

- ✓ Free-issue scope captured first: what the client supplies vs what the EPC installs can halve the apparent EPC cost
- ✓ GEOALT terrain upload: site area, slope, terrain class, interactive 3D viewer
- ✓ Scaling engine derives module, string, inverter and station counts; PVcase import replaces derived quantities with design data
- ✓ Save-draft, per-step validation, locked outputs with revisioning

38 person-days · Phase 1

B2 · Project Validation

Converts wizard output into a formal, governed project record before anything can progress.

- ✓ Draft promoted to a locked record with an auditable revision history
- ✓ Automated feasibility and compliance checks with a mandatory acknowledgement gate
- ✓ Technical sign-off routed to the responsible role

6 person-days · Phase 1

B2b · Risk Register & Provisions

The differentiator: every risk is priced as a named £ provision, not a blanket percentage, and flows into the budget as a visible line.

- ✓ Per-risk capture: category, status, likelihood, named £ provision, basis of estimate
- ✓ Categories: ground, information gaps, grid connection, planning, access and environment
- ✓ Confidence score dial with rule-based deductions

10 person-days · Phase 1

B3 · Product & Stock Calculator

The core engine: auto-generated bill of materials, priced from the rate library across 17 cost packages.

- ✓ Point-in-time rates, territory-specific, confidence flags, role-based ownership
- ✓ Free-issue deduction: supply cost zeroed, installation retained, both shown
- ✓ Location, ground, access and programme multipliers; inflation; contingency and margin
- ✓ Outputs: budget summary, full BOQ to Excel and PDF, assumptions register, sensitivity table, investor one-pager

38 person-days incl. exports · Phase 1

04 The delivery & governance workspace

PHASE 1 · REUSE, DO NOT REBUILD

B5 · Project & Phases Setup

The central delivery hub: phased plan, milestones, tasks, assignments and dependencies. Not built from scratch: it is delivered on Jobs Tracker, Coreproma's existing field-operations platform, already live in field service.

- ✓ Phased programme with milestones, owners and dependencies
- ✓ Solar projects extension: the only development work here, scoped and priced at discovery
- ✓ Subscription, per user per month, quoted with the seat count

Phase 1 · on Jobs Tracker · subscription + extension

B6 · Governance Tasks

Tracks each named provision through delivery: held, spent or released, closing the loop between the estimate and what actually happened.

- ✓ Live provision status against the B2b register
- ✓ Task execution and assignment run on Jobs Tracker alongside B5
- ✓ Risk-register integration through the platform's API, scoped at discovery

Phase 1 · included in the Jobs Tracker subscription

CROSS-CUTTING FOUNDATIONS · BUILT ONCE, USED EVERYWHERE · 25 PERSON-DAYS + 8 DISCOVERY + 22 QA AND GO-LIVE

Platform & DevOps
Azure infrastructure, database schema, CI/CD, Dev, Test and Prod environments

Identity & security
Entra ID SSO, MFA, role-based access, audit logging

Discovery, QA & go-live
Requirements sign-off, UX flows, system testing and UAT on the Hessay reference project

B4 · Supplier & third-party management

Pre-qualified suppliers submit offers against the project's bill of materials, inside a wider application for managing supply and third parties.

- ✓ Offer submission scored on price, lead time and ESG criteria
- ✓ Accepted prices feed back into the rate library and project budget
- ✓ Supplier onboarding, pre-qualification, compliance documents and performance: **new scope beyond the 20 days quoted for the portal alone, to be estimated at discovery**

20 p-days portal + new scope · Q1 2027

B7 · Reports

Live risk and cost exposure: which provisions are spent, which resolved, what remains.

- ✓ Essential estimate and summary export delivered in Phase 1
- ✓ Full dashboards and scheduled management and investor reports in Q1 2027

4 p-days Phase 1 · 14 p-days Q1 2027


05 Development plan & programme

ARITHMETIC, NOT PESSIMISM

7	18 Dec	2 or 3	Q1 27
MODULES LIVE IN PHASE 1, INCLUDING THE JOBS TRACKER WORKSPACE	GO-LIVE, THEN JANUARY HYPERCARE	DEDICATED PEOPLE, FULL WINDOW	SUPPLY, THIRD PARTY AND RATE INTELLIGENCE

Phase 1 requires a dedicated team of 2 or 3 across roughly sixteen weeks from signature. A single developer cannot hit December. The Jobs Tracker workspace itself is not in that figure, because it is not built: only its solar projects extension and the risk-register integration are development work, and both now sit inside Phase 1 rather than being deferred. That is why the four weeks gained by moving off mid-November do not read as float.

INDICATIVE PROGRAMME · CONTRACT SIGNATURE TO GO-LIVE

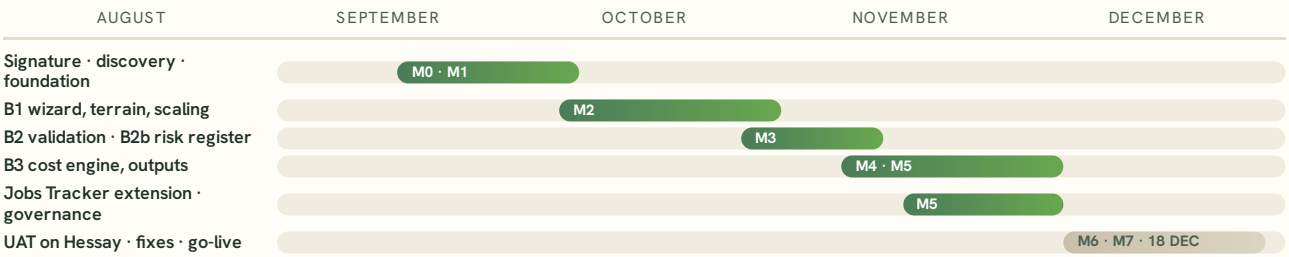

MILESTONES · EACH ONE IS AN ACCEPTANCE POINT

M0 · End August — SIGNATURE
Contract signature and mobilisation · every week of delay past this point moves go-live into January

M1 · Mid-September — FOUNDATION
Discovery signed off · Azure environments live · Entra ID SSO and MFA working · schema deployed

M2 and M3 · October — CAPTURE · RISK
B1 wizard captures a project end to end, demoable, with terrain upload and scaling engine · B2 validation and the B2b risk register with named provisions working

M4 and M5 · November — ENGINE
Cost engine produces an end-to-end estimate · outputs, Jobs Tracker extension and governance integration accepted · Phase 1 feature-complete

M6 and M7 · December — GO-LIVE
UAT on the Hessay dataset, then production go-live about 18 December, followed by a January hypercare window

06 Risks to the date, and what protects it

NAMED OWNERS, FIXED SCOPE

Rate data supplied late — HIGH
Mitigation: a data-handover deadline in the contract · build proceeds against placeholder rates in parallel · note that the QS and procurement team will be least available in late December

Scope creep, Q1 2027 work pulled into Phase 1 — HIGH
Mitigation: written scope freeze at the estimating core plus the Jobs Tracker workspace · change control for everything else · the proposed modules in Annex A are explicitly outside this contract

Terrain 3D and PVcase parsing complexity — MEDIUM
Mitigation: reuse of the existing 3D viewer, time-boxed, with a manual-entry fallback already in the design

Third-party API licensing lead time — MEDIUM
Mitigation: PVcase and Google Maps Platform keys ordered in Sprint 0

Key-person illness in a thin team — MEDIUM
Mitigation: a team of 2 or 3 rather than a lone developer · documented code and CI

What Ethical Power provides

- ✓ Rate library figures from the QS and procurement team by the end of August
- ✓ A nominated product owner for weekly reviews and UAT
- ✓ Entra tenant cooperation for application federation
- ✓ The Hessay dataset as the reference test project
- ✓ Third-party licences: PVcase, Google Maps Platform

What Coreproma commits

- ✓ A dedicated team of 2 or 3 for the full Phase 1 window
- ✓ Design decisions confirmed during discovery, Sprint 0
- ✓ Milestone acceptance before each payment stage
- ✓ Security review, documentation and training before cut-over

07 Infrastructure · Microsoft Azure hosting

ONE CLEAN MONTHLY COST

The platform runs in a Coreproma-managed Azure subscription: Coreproma provisions, secures, monitors and operates the environment; Azure consumption is re-billed monthly at cost. Data residency is UK South, with Dev, Test and Production environments isolated from one another and automated Azure SQL backups with point-in-time restore.

App Service, Linux
Wizard front end and the application and API tier, with a staging slot

Azure SQL Database
Rate library, project records, risk register, revisions

Blob storage
GEOALT and PVcase uploads, generated BOQ, PDF and Excel outputs

Storage queues + workers
Terrain parsing, PVcase import, BOQ generation: heavy jobs retried safely off the web request

Key Vault
Connection strings, API keys, certificates

Application Insights
Uptime, performance, error tracking, audit

UK South
DATA RESIDENCY IN THE UNITED KINGDOM

3
ISOLATED ENVIRONMENTS · DEV, TEST, PRODUCTION

PITR
AZURE SQL POINT-IN-TIME RESTORE, DOCUMENTED RECOVERY

08 Address, certificates & sign-in

YOUR IDENTITY, YOUR CONTROL

One published address anchors everything
app.corepproma.io, or a delegated Ethical Power subdomain: the TLS certificate and the Entra redirect URL both bind to it.

HTTPS only, managed certificate
TLS 1.2+, HSTS, automatic renewal. No unencrypted access to the application.

Sign-in through Ethical Power's own Entra ID
Corporate Microsoft accounts, single sign-on, no separate password store. Access is granted and revoked by Ethical Power's IT; a leaver loses access immediately.

Who can sign in Only users granted the enterprise application in Ethical Power's Entra directory · provisioned and de-provisioned by Ethical Power IT	CLIENT-CONTROLLED
Credentials Ethical Power's own corporate identities, single sign-on · Coreproma stores no passwords	SSO
Control and offboarding A leaver removed in the directory loses application access immediately · no separate account clean-up	IMMEDIATE

MFA enforced · recommended

Every user completes multi-factor authentication on sign-in, enforced by a Conditional Access policy.

- ✓ Closes the single most common account-compromise route
- ✓ Costs nothing to build: configuration, not development

MFA not enforced by the app · not advised

Sign-in security is left to whatever policy exists in the tenant.

- ✓ Acceptable only if equivalent controls are already enforced tenant-wide
- ✓ For a tool that holds tender pricing, an un-enforced posture is weak

Also included: role-based access on a least-privilege basis (only QS and procurement roles can change rates), encryption in transit and at rest, audit logging of rate changes and approvals, UK data residency, patching, backups and a documented recovery procedure.

09 Updates & enhancements after go-live

CORRECTIVE VS NEW, KEPT SEPARATE

1. **Included in support**
   Bug fixes, security patches, minor tweaks and configuration changes within the existing scope.
2. **Change request** CHARGEABLE
   New features estimated in person-days, quoted, approved, then scheduled at the agreed day rate.
3. **Enhancement retainer** OPTIONAL
   A fixed block of development days per month, drawn against a prioritised backlog.

Q1 2027: supplier & third-party management, full reporting
France & Spain rate territories
Rate intelligence: commodity indices + supplier quotes
Reference projects beyond Hessay
Additional output templates

The B5 and B6 workspace evolves with the Jobs Tracker product under its subscription: its roadmap is Coreproma's, not change-controlled here.

10 Support & maintenance contract

12-MONTH TERM, RENEWABLE

Included	Standard	Enhanced
Support hours	UK business hours	**+ priority queue**
Hosting operation, monitoring, patching, backups	Yes	Yes, + periodic DR test
Bug fixes	Yes	**Faster SLA**
Minor updates / small changes	Limited allowance	Larger monthly allowance
Enhancement days included	None, chargeable	Small monthly block
Indicative fee	**Quoted with the tier**	**Quoted with the tier**

Severity	Definition	Response	Target restore
P1	Platform down, no user can work	Same business day	Best effort, priority
P2	Major function unavailable, no workaround	1 business day	3 business days
P3	Minor function impaired, workaround exists	2 business days	Next release
P4	Cosmetic, question, request	3 business days	Backlog

Exact SLA figures are confirmed with the chosen tier. Azure consumption is billed separately as a pass-through, except for the six months included under the capped route.

11 The proposed commercial structure

ONE ROUTE, CAPPED

Platforms of this kind change while they are being built: rate structures move, outputs get reshaped once real tenders run through them, and the first live estimates always suggest improvements. Rather than quote a range and invoice the difference, Coreproma proposes a single route. A new jointly-held structure owns the platform IP, and in exchange the development cost is capped. Currency GBP.

Shared ownership, capped development

£250,000

Hard cap on Phase 1 development, including six months of Azure hosting from go-live

- ✓ Comparable builds of this scope are normally **open-ended**: billed as the work evolves, with no ceiling on what the client finally pays. This one has a ceiling, and Coreproma carries everything above it
- ✓ Six months of hosting from go-live is included, covering the period in which development continues. Azure is billed at cost thereafter
- ✓ Requires the ownership structure described in Section 12: the platform is held jointly, not licensed and not sold outright
- ✓ The same capped approach is offered for the software required by the EcoGrid Resort project, scope to be defined separately
- ✓ The cap holds against the scope described in this document. Changes beyond it run through change control
- ✓ Support and maintenance are quoted separately against the chosen tier, Section 10

⚑ What the cap does, stated plainly. It fixes Ethical Power's development cost and moves the overrun risk to Coreproma. That is deliberate, and it is the consideration for shared ownership. It works only if the scope baseline is written down and change control is real: an uncapped scope behind a capped price is the one combination that fails for both sides.

12 Ownership of the platform

ONE STRUCTURE, JOINTLY HELD

Coreproma proposes a single ownership route rather than a menu. A new jointly-held structure owns the intellectual property in the developed estimation platform, and that shared ownership is what makes the capped price possible. Ethical Power's own data, its rate library figures, projects and estimates, always belongs to Ethical Power regardless of structure.

What the structure holds

A new entity, jointly held by Ethical Power and Coreproma, owns the IP in the bespoke estimation platform.

- ✓ The developed modules: creation wizard, validation, risk register, cost calculator, exports, and the Q1 2027 supplier and reporting work
- ✓ Neither party can commercialise the platform unilaterally; decisions sit with the structure
- ✓ Coreproma's pre-existing background IP and generic components are contributed or licensed in, and must be separated from the newly written foreground code in the contract
- ✓ Third-party licences, for example PVcase and mapping, are never assignable by Coreproma

What each side is trading

The structure is the consideration for the cap. Both sides give something up.

- ✓ **Ethical Power** gains cost certainty at £250,000 and a share of an asset it helped specify, instead of exclusive ownership of the code
- ✓ **Coreproma** absorbs build cost above the cap and gives up the right to resell the platform freely, in exchange for a continuing interest in it
- ✓ Still to be agreed: shareholdings, what each party contributes, governance and deadlock, what happens on exit, and how the EcoGrid Resort software sits inside the same structure

⚑ **This is a corporate transaction, not a payment term.** None of the terms in the last bullet above are agreed, and they cannot be settled inside a development contract. This section is offered as heads of terms to be negotiated in parallel with the build contract, not as a settled deal. Because it is now the only route proposed, drafting those heads of terms sits on the critical path to signature, not after it.

HEADS OF TERMS TO BE AGREED, IN PARALLEL WITH THE BUILD CONTRACT

Shareholdings and contributions — FIRST
Who holds what proportion, and whether Coreproma's pre-existing background IP is contributed to the structure or licensed into it. The two are not the same and are valued differently

Governance and deadlock — TERMS
Board composition, reserved matters requiring both parties, and what happens when the parties disagree on the roadmap

Commercialisation — TERMS
Whether the structure may license the platform to other EPC contractors, on whose initiative, and how any proceeds are shared

Exit and continuity — TERMS
What happens to the platform if either party leaves or is sold, and whether source-code escrow is required for Ethical Power's operational continuity

Scope of the structure — SCOPE
Whether the EcoGrid Resort software sits inside the same structure or alongside it under a separate capped arrangement

⚑ **Jobs Tracker carve-out.** The delivery and governance workspace, B5 and B6, runs on Jobs Tracker, Coreproma's pre-existing field-operations product. Jobs Tracker and its solar projects extension sit **outside** the new structure: they are never assigned to it or to Ethical Power, and are provided under the per-user monthly subscription for as long as the service is used. The structure above covers the bespoke estimation platform only.

13 Scope, effort & payment schedule

ONE ENVELOPE, ONE CAP

The table below is the scope and effort behind the envelope in Section 11. Effort figures are Corepproma's estimate. Currency: GBP. Items marked **at discovery** are real scope with no estimate yet, not free: they are sized in Phase 0 and confirmed in writing before work starts.

Item	Basis	Effort (p-days)
Phase 0 · discovery & design	One-off	8
Foundation, DevOps, identity & security	One-off	25
B1 creation wizard	One-off	38
B2 validation	One-off	6
B2b risk register & provisions	One-off	10
B3 calculator + outputs	One-off	38
B7 essential reporting output	One-off	4
QA, UAT & go-live	One-off	22
Phase 1 bespoke development, sub-total	**One-off**	·
Jobs Tracker workspace, B5 + B6 · Phase 1	Subscription	·
Jobs Tracker solar projects extension & governance integration · Phase 1	One-off	at discovery
Q1 2027 · supplier & third-party management	One-off, later	20 + new scope
Q1 2027 · full B7 management & investor reporting	One-off, later	14
Q1 2027 · rate intelligence, commodity indices + supplier quotes	One-off, later	at discovery
Azure hosting, managed	Monthly	·
Support & maintenance	Monthly	·

PAYMENT SCHEDULE · £250,000 CAPPED TOTAL

Induction fee, on signature — £60,000
Mobilisation · M0 · credited as part of the capped total

70% of the balance, on delivery of the first module — £133,000
Production go-live of the estimating core accepted · M7 · about 18 December 2026

30% of the balance, Q1 2027 — £57,000
Alongside the supplier and procurement module and the rate-intelligence work

Total under the cap — £250,000
Including six months of Azure hosting from go-live

⚑ **One reading to confirm before issue.** The schedule above credits the £60,000 induction fee against the capped total and applies 70/30 to the £190,000 balance, which sums to exactly £250,000. Read literally as sixty thousand *plus* 70% *plus* 30% of the total, the schedule would sum to £310,000 and break the cap. Confirm which is intended before this document is issued.

This quotation is valid for 30 days from its date of issue. Effort estimates are indicative and firmed up at the end of discovery, Phase 0.

14 Assumptions, exclusions & dependencies

NO SURPRISES LATER

Key assumptions

- ✓ Contract signature by end August 2026, with a dedicated team of 2 or 3 for Phase 1
- ✓ Ethical Power supplies rate-library figures, a product owner, Entra tenant cooperation and the Hessay reference dataset
- ✓ Phase 1 scope is frozen at the estimating core, essential reporting output, and the Jobs Tracker workspace with its solar projects extension
- ✓ The B5 and B6 workspace is provided on Jobs Tracker under a separate per-user monthly subscription; seat count and minimum term to be confirmed
- ✓ Go-live is mid-December with a January hypercare window; no UAT or cut-over activity is planned between 22 December and 2 January

Exclusions · not in the priced development

- ✓ Azure consumption: pass-through, billed monthly
- ✓ Third-party licences: PVcase, Google Maps Platform, commercial data feeds
- ✓ Grid-connection cost modelling: excluded by design, obtained from the DNO
- ✓ Rate data population: the responsibility of Ethical Power's QS and procurement team
- ✓ Data migration beyond the Hessay reference project, and any hardware
- ✓ Everything in Annex A: the proposed investor portal and site capture modules are indicative only and form no part of this quotation
- ✓ Drone flight operations of any kind: see Annex A, Module 2

15 Next steps

SIGNATURE TO GO-LIVE IN ABOUT 16 WEEKS

1

Coreproma confirms

The cost envelope and payment schedule are confirmed, and the reading of the induction fee is settled.

2

Ethical Power selects

Approval of the shared ownership structure in principle, the MFA option, the support tier, and the Jobs Tracker subscription basis: seats and minimum term.

3

Both parties confirm

The Phase 1 scope freeze, the rate-data handover date, and a start date for drafting the heads of terms for the new structure.

4

Signature, then build

Contract signature by end August, discovery immediately after, go-live about 18 December 2026.

The one-line version

- ✓ A working, risk-priced estimating engine live before the year ends
- ✓ Delivery and governance on a proven platform, by subscription, in the same phase
- ✓ Every price visible, every payment tied to acceptance
- ✓ Our data always ours; ownership shared, and the cost capped because of it

A Annex A · Proposed additional modules

INDICATIVE ONLY · NOT PRICED

⚑ **This annex is not part of the quotation.** Neither module is scoped, estimated or priced, neither is included in Phase 1 or in the Q1 2027 work, and nothing here forms part of what Ethical Power is being asked to approve. Both are recorded so the direction is visible early. If either is wanted, it is scoped and quoted separately, after the estimating core is live.

Module 1 · Investor portal

Projects carrying third-party investors, as with the French project, need those investors to see the documents relevant to an investment decision and the reports produced as the project proceeds.

- ✓ Cheaper than it looks: the platform already produces what an investor needs, the named risk provisions, the budget and sensitivity table, the investor one-pager and live cost exposure. The portal is a permissioned external role over existing data plus a document register, not a second application
- ✓ Least privilege by project: an investor sees only the project or SPV they are in
- ✓ A hard boundary around what never leaves: tender pricing, margin and the rate library
- ✓ Watermarking and an access log, giving an immutable record of what was disclosed and when, which is the part that matters in a dispute

Module 2 · Site capture

Mission-planned drone capture of a site, with the imagery landing on the project record: terrain for the wizard, dated evidence against risk provisions, and progress for reporting.

- ✓ Planning software only, on Coreproma's existing WaypointsCreator platform: survey grids, 3D terrain simulation, obstacle detection and mission export to DJI controllers
- ✓ Imagery and orthomosaics attach to the project record and feed the Step 2 terrain model, replacing a separate topographic survey upload
- ✓ **Flight operations are excluded, deliberately.** Commercial site survey flying in the United Kingdom is a Specific category activity: it needs a CAA Operational Authorisation, a certified remote pilot and third-party insurance under EC 785/2004. Those obligations sit with whoever flies, Ethical Power or its surveyor, not with Coreproma
- ✓ Commercial basis would be the existing WaypointsCreator per-seat subscription plus integration work

WHAT WOULD HAVE TO BE SETTLED BEFORE EITHER MODULE IS QUOTED

The investing entity and its jurisdiction — MODULE 1

United Kingdom or France · disclosure duties toward investors differ, and the answer shapes the design rather than decorating it. Legal review before build, not after

A role on the estimation platform, or a separate application — MODULE 1

The cost difference is large. A permissioned external role reuses everything; a separate application duplicates identity, hosting and document handling

Who holds the Operational Authorisation and the insurance — MODULE 2

No flying happens under this platform until that is named in writing. Coreproma supplies planning software, not aviation services

A named sponsor and a confirmed use case for each module — BOTH

Both are recorded here because they are possible. Neither should be built because it is possible
